
Las Vegas Stadium Authority

Financial Summary

July 2020

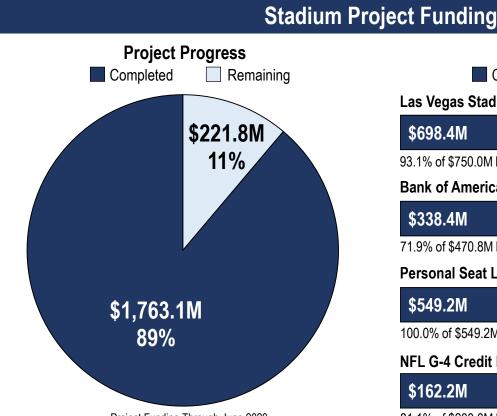

Project Funding Through June 2020 Project Budget = \$1.98 Billion (includes \$14.9 million for third-party activations)

. . ..

Funding Sources Completed Remaining Las Vegas Stadium Authority \$698.4M 93.1% of \$750.0M budget

Bank of America Senior Credit Facility

\$338.4M

71.9% of \$470.8M budget*

Personal Seat License Revenue

\$549.2M


100.0% of \$549.2M budget*

NFL G-4 Credit Facility

\$162.2M

81.1% of \$200.0M budget

* Reflects adjustment for additional PSL sales revenue

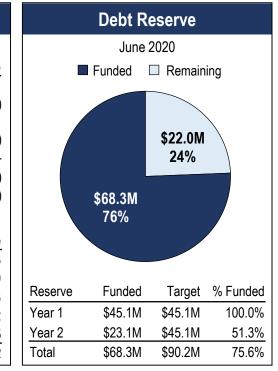

Notes: 1 Room tax revenue reflects preliminary data on room tax accruals; 2 Operating budget funded by monthly distribution of 1/12 of annual budgeted total; 3 Figures are estimates and subject to change; ⁴ Expenses reflect month they are incurred.

Stadium Authority Finances

nd Allocated Uses		
Total to Date	FY20 Budget	Remaining Balance
\$36,089,139	\$49,550,000	(\$13,460,861)
\$1,887,149	\$2,166,640	(\$279,491)
\$33,978,750	\$33,978,750	\$ -
\$218,241	\$9,000,000	(\$8,781,759)
\$ -	\$4,404,610	(\$4,404,610)
xpenses⁴		
Total to Date	FY20 Budget	Remaining Balance
\$430,078	\$600,000	\$169,923
\$33,000	\$36,000	\$3,000
\$175,127	\$210,000	\$34,873
\$57,678	\$115,000	\$57,322
\$23,625	\$1,205,640	\$1,182,015
\$719,508	\$2,166,640	\$1,447,132
	\$36,089,139 \$1,887,149 \$33,978,750 \$218,241 \$ - xpenses⁴ <u>Total to Date</u> \$430,078 \$33,000 \$175,127 \$57,678 \$23,625	Total to Date FY20 Budget \$36,089,139 \$49,550,000 \$1,887,149 \$2,166,640 \$33,978,750 \$33,978,750 \$218,241 \$9,000,000 \$- \$4,404,610 xpenses4 FY20 Budget Total to Date FY20 Budget \$430,078 \$600,000 \$33,000 \$36,000 \$175,127 \$210,000 \$57,678 \$115,000 \$23,625 \$1,205,640
